



Ogden Canyon 36" Water Transmission Pipeline PHASE 1 | REPLACEMENT PROJECT

PROJECT TIMELINE – JULY 28, 2025 – MAY 1ST, 2026

Work Days: Monday - Friday, Saturday as necessary

Work Hours: Sunrise - Sunset

- Access to properties will be maintained but may be restricted briefly during daytime hours. Please contact project hotline for coordination.
- Excavated regions along pipeline ROW will be backfilled nightly.
- Schedules are subject to change due to weather and materials available.

Oct. 13, 2025 – May 1, 2026

Pipeline installation begins at the Fairmount vault, moving east along the ROW.

Cobbles

Heavy Fill Area

July 28, 2025 – Sept. 15, 2025

Remove/relocate material over pipeline.

Aug. 18 – 30, 2025

Transport heavy equipment across County Bridge at West Hermitage. NOTE: Clear and grub entire pipeline ROW in region 1 & 2.

Oct. 1, 2025 – Nov. 5, 2025


Using a crane, transport new pipeline segments across river from staging area (east of Hermitage Bridge) and transport to planned areas along Region 1.

Oct. 1, 2025 – Nov. 5, 2025

Transport new pipeline segments across from staging area (east of Alaskan Inn) and transport to planned areas along Region 2.

Nov. 1, 2025 – May 1, 2026

Pipeline installation begins just west of Valhalla, moving west along the ROW.

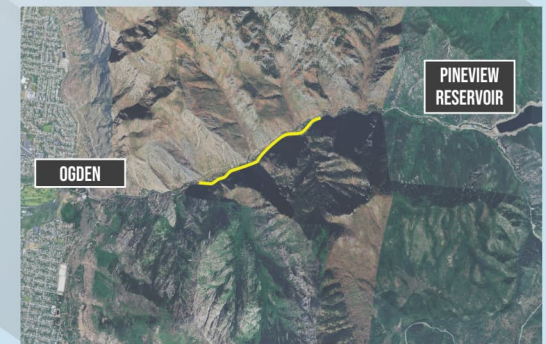

info@ogdencitypipeline.com · 801.838.8365 · ogdencitypipeline.com

