



# Ogden Canyon 36" Water Transmission Pipeline PHASE 2 · REPLACEMENT PROJECT


## PROJECT TIMELINE: JULY 28, 2025 - MAY 1ST, 2026

Work Days: Monday - Friday, Saturday as necessary

Work Hours: Sunrise - Sunset

- Access to properties will be maintained but may be restricted briefly during daytime hours. Please contact project hotline for coordination.
- Excavated regions along pipeline ROW will be backfilled nightly.
- Schedules subject to change due to weather and materials available.

Pipeline project

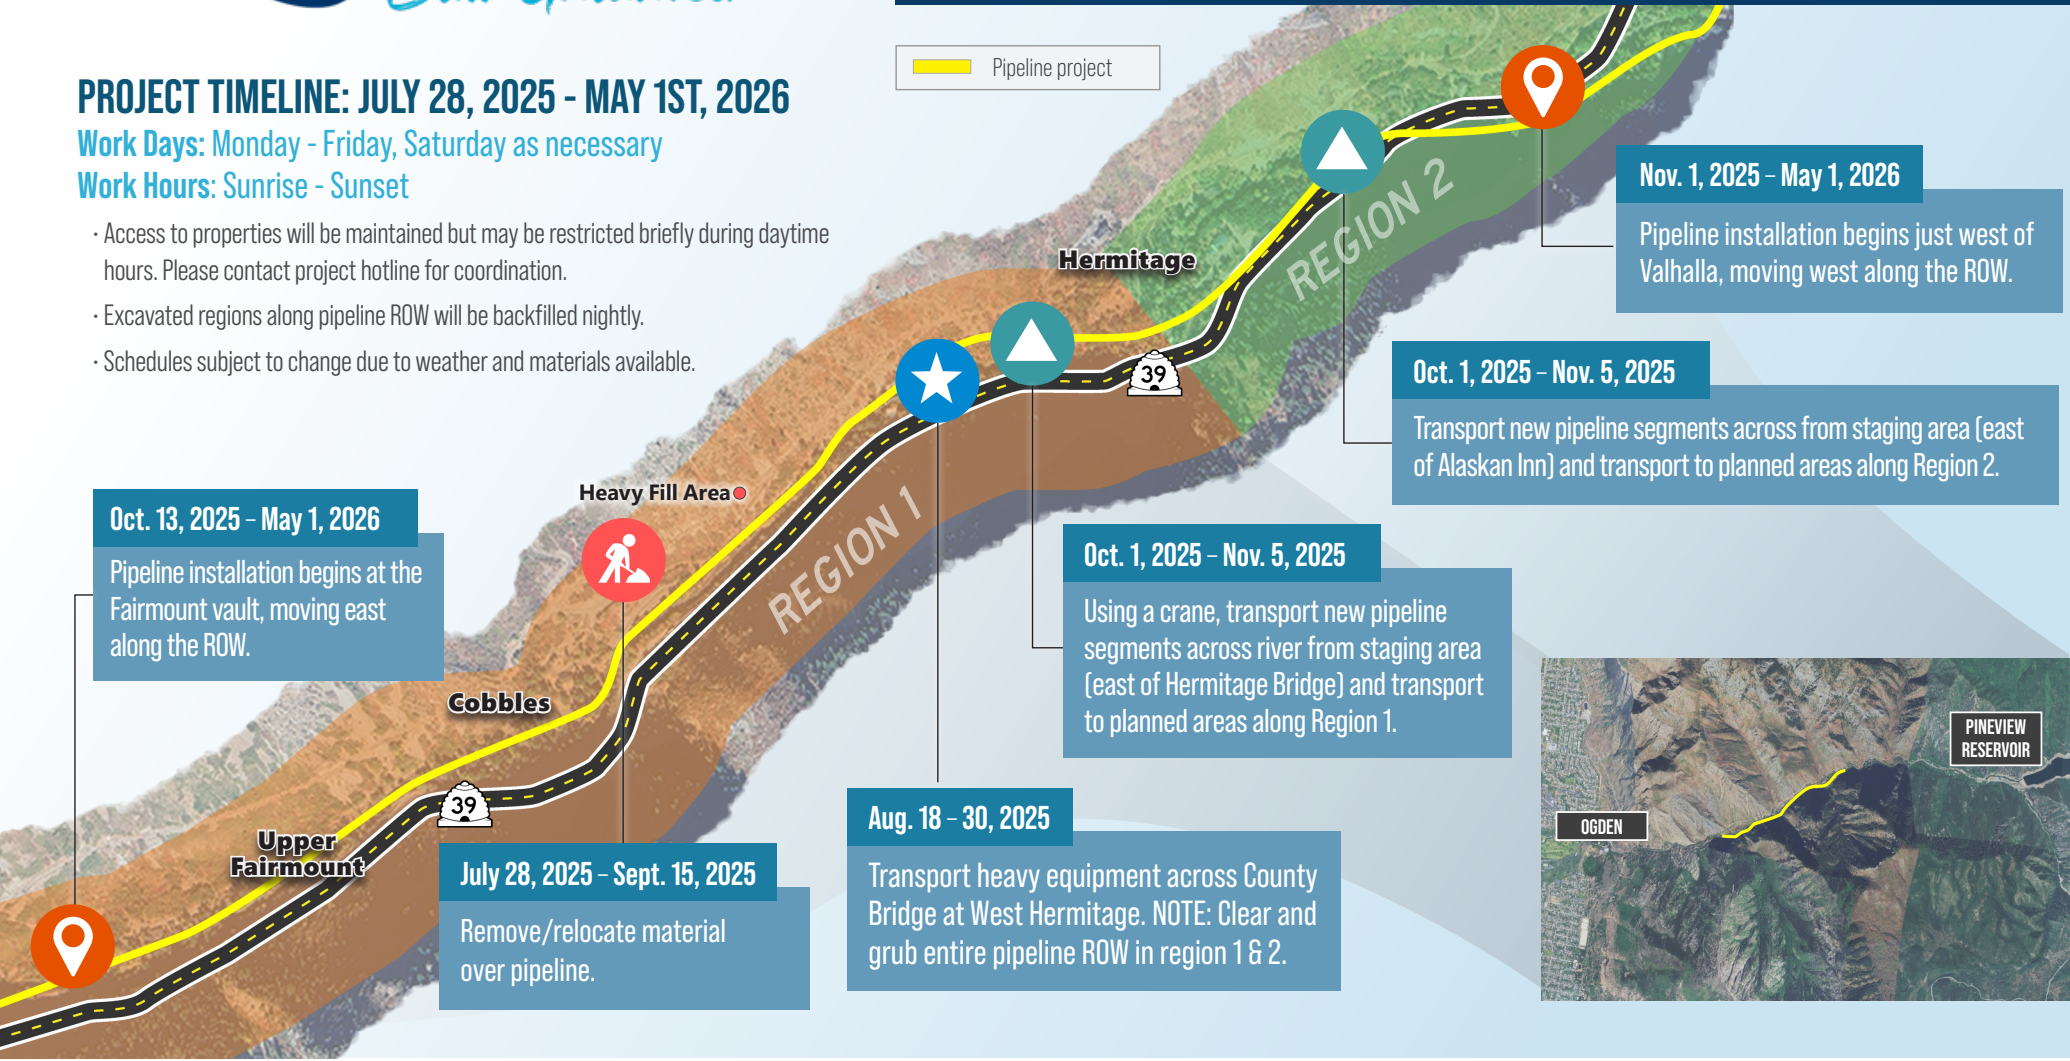

**Oct. 13, 2025 - May 1, 2026**  
Pipeline installation begins at the Fairmount vault, moving east along the ROW.

**July 28, 2025 - Sept. 15, 2025**  
Remove/relocate material over pipeline.

**Aug. 18 - 30, 2025**  
Transport heavy equipment across County Bridge at West Hermitage. NOTE: Clear and grub entire pipeline ROW in region 1 & 2.

**Oct. 1, 2025 - Nov. 5, 2025**  
Using a crane, transport new pipeline segments across river from staging area (east of Hermitage Bridge) and transport to planned areas along Region 1.

**Oct. 1, 2025 - Nov. 5, 2025**  
Transport new pipeline segments across from staging area (east of Alaskan Inn) and transport to planned areas along Region 2.

**Nov. 1, 2025 - May 1, 2026**  
Pipeline installation begins just west of Valhalla, moving west along the ROW.

